


BMDA-12

 Project : BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH.						Well No.: District: Barisal Upazilla: Barisal Union: Barisal Mouza: Barisal J.L. No: 57 Plot No: 516
Engineer Barind Multipurpose Development Authority			Drilling Contractor A. M. A. ENTERPRISE			
Date started 31.12.06 7.00 hrs; Date completed 31.12.06 7.00 hrs. Logged by SAE ; Rod length 0 ft.						
Drilling time log			Graphic log	Thickness (ft.)		Description of formation
rod	from	to		from	to	
1	7.00			0	10	log.
				20		
					30	
					40	
					50	
					60	
					70	
					80	
					90	
					100	
22	7.00			10	20	1st layer Gravel
						2nd layer Gravel
						
						
						
						
						

SSAE/SAE

Date

৩১ ডিসেম্বর ২০০৬

C-7-BMDA2-252 (0.0)

Asstt. Engr.

Date

৩১ ডিসেম্বর ২০০৬, জাতিসংঘ জোন


For the Contractor

Date

৩১ ডিসেম্বর ২০০৬

 Project : BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAHI		Well No. : District : Rajshahi Thana : Autoary Union : Balarampur Mouza : anlongh J.L. No. : 57 Plot No. : 516
Engineer : BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY	Drilling Contractor : A. Kalam Enterprise.	CONSTRUCTIONS DETAILS

Operation	Date	Started	Date	Completed
Drilling	3/12/06	7.00 HRS	3.12.06	9.00 HRS
Casing		HRS		HRS
Gravel Placing	-DC-	20.00 HRS	-DC-	22.00 HRS
Drilling diameter 22" / 24" / 44" Casing Pipe (Dia 14") mild steel UWC 6m ft. above GL UWC (incl. Reducer) 32.74m ft. below GL Lapping 1.5m Total length [ft] 33.34m L.W.C. (Dia inch) mild steel Depth below GL From to Length [ft] From to Total length [ft] Screen (8) inch slot, stainless steel/FG Dia 6"/8"/14" Depth below GL From 32.74m to 61.98m Length [ft] 29.24m From to Lapping 76m Total length [ft] 29.24m Bailplug (Dia 8"") Depth below GL From 61.98m to 62.97m Centralizers Lapping 6m. Depth below GL at 112/132/152/172/192/209m. Total Numbers 6 Gravel Gravel quantity (approx) 15.83 Cum. cft. Depth below GL From 0 to 200.4 Length [ft] 15.83 cft. Fixture length from top of UWC to bottom of Bail plug 63.57m Verticality test max. deviation 1.62m inch at 100m ft Depth Date 3/12/2006 Material used: h/p with Reducer, Screen, Bail Plug 34.34+30.99=65.33m Lapping 1.5m+76=2.26m.				

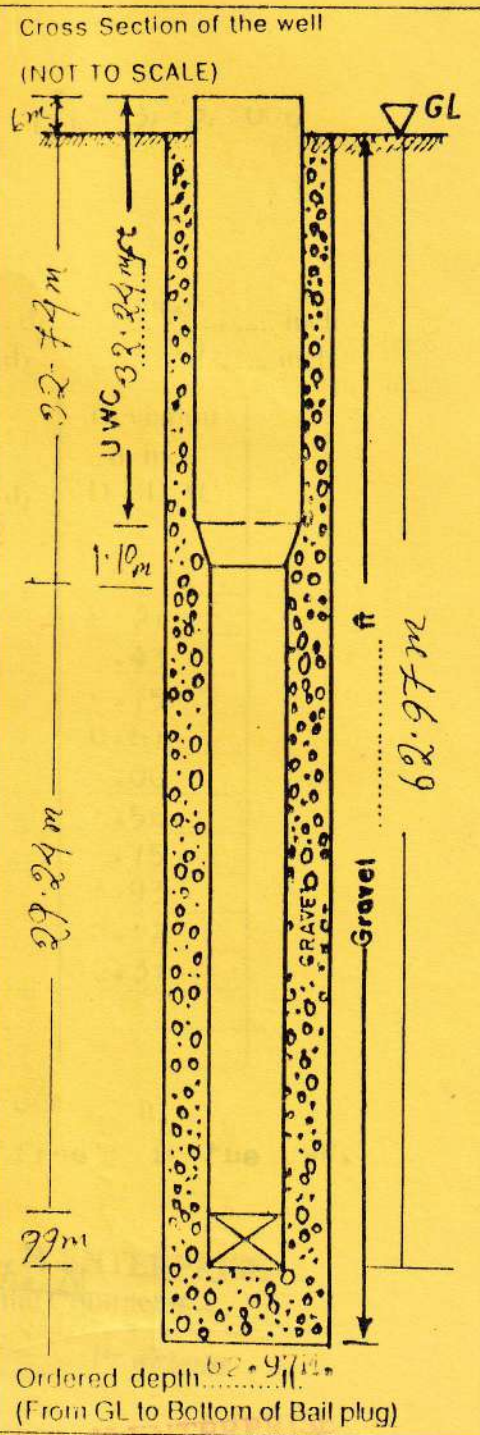

SAE/Sr. SAE

Date:

Asstt. Engineer

Date:

For the Contractor

Date:



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH

INSPECTION OF VERTICALITY OF THE TUBEWELL

Before Shrouding

- Well No.:
- District: Barisal
- Upazilla: Autarg
- Union: Belarampur
- Mouza: Kalomagh
- J.L. No.: 57
- Plot No.: 516
- Total Length of the Tubewell: 209'-4"
- Length of UWC (Excluding Reducer): 10' ft. Date: 31/12/2006
- Name of Sinking Contractor: A. Kalam Enterprise.

VERTICALITY DATA SHEET

Suspension Height (H) 10' ft. Dia of UWC, d_1 4.00 inch
Dia of Disc, d_2 3.5 inch

Depth in ft. L.	Deviation in inch X	Bearing Reading Pointing North	Calculated Deviation in inch $D = \frac{X(L+H)}{H}$	Disc Factor $C = \frac{d_1-d_2}{2}$	Deviation in inch $D + D \cdot C$
10'	1/16	Est	0.12	0.25	0.31
20'	1/16	-	0.24	"	.43
30'	2/16	-	0.5	"	0.75
40'	2/16	-	0.62	"	0.81
50'	2/16	-	0.75	"	1.00
60'	3/16	-	1.31	"	1.56
70'	3/16	-	1.5	"	1.75
80'	3/16	-	1.68	"	1.93
90'	3/16	-	1.87	"	2.12
100'	3/16	-	2.06	"	2.31
110'					
120'					

11. Maximum Deviation: 2.31 inch at depth 100' ft.
12. Other observation, if any: Dolly passed up to depth 100' from top of the UWC.

SSAE/SAE
Date

Asstt. Engr. সফিকুল ইসলাম
Date সহকারী প্রকৌশলী
বিএমডিএ, ইউনিট-২, আটোয়ারী জোন
আটোয়ারী, পঞ্চগড়

K. H. ENTERPRISE
For the Contractor
Date Proprietor



**BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH**

INSPECTION OF VERTICALITY OF THE TUBEWELL

After Shrouding

1. Well No. :
2. District : **Panchagore**
3. Upazilla : **Arao**
4. Union : **Balarampur**
5. Mouza : **Kalamagn**
6. J.L. No. : **57**
7. Plot No. : **516**
8. Total Length of the Tubewell : **209'-4"**
9. Length of UWC (Excluding Reducer) **110'** ft. Date : **3/12/2006**
10. Name of Sinking Contractor : **Kalam Enterprise.**

VERTICALITY DATA SHEET

Suspension Height (H) **10'** ft. Dia of UWC, d_1 **14.00** inch
Dia of Disc, d_2 **13.5** inch

Depth in ft. L.	Deviation in inch X	Bearing Reading Pointing North	Calculated Deviation in inch $D = \frac{X(L+H)}{H}$	Disc Factor $C = \frac{d_1 - d_2}{2}$	Deviation in inch $D = D' + C$
10'	0	was ⁺	0	0.5	0.5
20'	0	-	0	"	0.5
30'	1/16	-	0.25	"	0.5
40'	1/16	-	0.31	"	0.56
50'	1/16	-	0.37	"	0.62
60'	2/16	-	0.67	"	1.12
70'	2/16	-	1.00	"	1.35
80'	2/16	-	1.2	"	1.37
90'	2/16	-	1.25	"	1.5
100'	2/16	-	1.37	"	1.62
110'					
120'					

11. Maximum Deviation : **1.62** inch at depth **100'** ft.
12. Other observation, if any :
13. Straightness : Dolly passed upto **100'** ft. freely in the UWC.

SSAE/SAE

Date

Assut. Engr. (সহকারী প্রকৌশলী)

Date

K. ENTERPRISE
For the Contractor.

Date

Proprietor



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

DEVELOPMENT RECORD (Period : 2 hour)

Page No : 1

Date: 5/12/2006
Starting Time 7 hrs 0 minute, Capacity of Pump 3.00 cusec
Ref. Mark (Top of Housing) 2'-0" ft. above G.L.
Static Water Level 10'-0" ft. below top of Housing Pipe
Size of Orifice 6 inch, Size of Delivery Pipe 5 inch
Length of UWC 100' ft. Depth of Pump Setting 33 ft.

Well No :
District : Faridkot
Upazilla : Faridkot
Union : Faridkot
Mouza : Faridkot
J.L. No : 5
Plot No : 1

Time	Piezometric Height (inch)	Discharge (cusec)	Pumping Water Level below Reference Mark (ft.)	Actual Draw-Down (ft.)	Remarks
00mn (8 hrs)	13.5	1.02	10'-0"	SWL	50% Discharge
05 mn			21'-0"	11'-0"	
10 mn			21'-3"	11'-3"	
15 mn			21'-5"	11'-5"	
20 mn			21'-6"	11'-6"	
25 mn			21'-7"	11'-7"	
30 mn			21'-7 1/2"	11'-7 1/2"	
35 mn	53"	2.00	32'-0"	22'-0"	100% Discharge
40 mn			32'-4"	22'-4"	
45 mn			32'-6"	22'-6"	
50 mn			32'-7"	22'-7"	
55 mn			32'-8"	22'-8"	
60 mn			32'-9"	22'-9"	
65 mn			32'-10"	22'-10"	
70mn	84"	2.5	38'-1"	28'-1"	125% Discharge
80 mn			38'-5"	28'-5"	
90 mn			38'-6 1/2"	28'-6 1/2"	
100 mn	113"	3.00	44'-0"	34'-0"	150% Discharge
110 mn			44'-2"	34'-2"	
120 mn (2 hrs.)			44'-3"	34'-3"	

1 cusec = 28.32 LPS.

S SAE/SAE

Date

Asstt. Engr.

Date

For the Contractor

Date

Proprietor

C-10-BMDA2 118 (P-2)



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAISHAH

RECOVERY RECORD
(Period : 1 hour)

Page No : 2

5/12/2006

Date: ~~5/12/2006~~

Starting Time 9 hrs 0 Minute

Ref. Mark (Top of Housing) 2'-0" ft. above G.L.

Static Water Level 10'-0" ft. below top of Housing Pipe

Well No.
District **Barisal**
Upazilla **Autoary**
Union **Salarampur**
Mouza **Salomagh**
T.L. No. **21**
Plot No. **10**

Time	Water Level below Reference Mark (ft.)	Remarks
00mn (2 hrs)	44'-3"	
01 mn	13'-5"	
02 mn	12'-9"	
03 mn	12'-3"	
04 mn	11'-9"	
05 mn	11'-6"	
07 mn	11'-4"	
09 mn	11'-2"	
11 mn	11'-0"	
13 mn	10'-10"	
15 mn	10'-8"	
20 mn	10'-7"	
25 mn	10'-6"	
30 mn	10'-5"	
40 mn	10'-4"	
50 mn	10'-3"	
60 mn (3 hours)	10'-2"	

S.SAE/SAE

Date

Asstt. Engr (সহকারী ইঞ্জিনিয়ার)

Date **সকালী প্রকৌশলী**

বিত্তমতি, বর্ডা ট-২, আটোরাগী জেজ
আটোরাগী, পঞ্চদু।

K. H. ENTERPRISE

For the Contractor

Date **Proprietor**

C-10-RMDA2-1181P-4)

বিত্তমতি, বর্ডা ট-২, আটোরাগী জেজ

আটোরাগী পঞ্চদু



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAISHAH

SAND TEST RECORD (Period : 1 hour)

Page No : 3

Date: 5/12/2006	Well No
Starting Time 10 hrs. 0 minute, Capacity of Pump 5.00 cusec	District Barisal
Ref. Mark (Top of Housing) 2'-0" ft above G.L.	Upazilla Artoary
Static water level 10'-0" ft below top of Housing Pipe.	Union Balarampur
Size of Orifice 6 inch, Size of Delivery Pipe 5 inch	Mouza Kalomagi.
Length of UWC 100 ft, Depth of Pump setting 63 ft.	J.I. No 57
	Plot No 56

Time	Pumping Water Level below Ref. Mark (ft)	Sand Content
00mn (3 hrs)	10'-2"	
01 mn	43'-0"	
02 mn	43'-2"	
03 mn	43'-3"	
04 mn	43'-4"	
05 mn	43'-5"	
07 mn	43'-6"	
09 mn	43'-7"	
11 mn	43'-8"	
13 mn	43'-9"	
15 mn	43'-10"	
20 mn	43'-11"	
25 mn	44'-0"	
30 mn	44'-1"	
40 mn	44'-2"	
50 mn	44'-3"	
60 mn (4 hrs.)	44'-4"	

N.B.

Accepted Sand Content after 5 minutes
100 ppm and after 10 minutes-30 ppm.

Observed Result :

(a) After 5 minutes : 25 ppm

(b) After 10 minutes : 110 ppm

SSAE/SAE

Date

Asstt Engr.

Date

K. HENERPRISE

For the Contractor

Date

Proprietor

C-5 BMDA-001 (P-2)

(স্বাক্ষরিত ইস্তাফা)
স্বাক্ষরিত ইস্তাফা
বিদ্যমান, ৫৬-৮-২, আটোয়ারী জোন
আটোয়ারী, বরগুনা



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

Development Records
(Period : 4 hours)
150 % Discharge

Page No : 4

Date: 5/12/2006		Well No :
Starting Time 11 hrs 00 minute, Capacity of Pump 3.00 cusec	District :	Rajshahi
Ref. Mark (Top of Housing) 2'-0" ft above GL.	Upazilla :	Antony
Static Water Level 10'-0" ft below top of Housing Pipe.	Union :	Balaranpur
Size of Orifice 6 inch, Size of Delivery pipe 5 inch	Mouza :	Kalouagh
Length of UWC 110 ft, Depth of Pump Setting 83 ft	JL No :	57
	Plot No :	56

Time	Piezometric height (ft)	Discharge (cusec)	Pumping Water Level below Ref Mark (ft)	Actual Draw-Down (ft)	Remarks
00mn (4 hrs)	113"	3.00	44'-4"	31'-4"	Back Wash only one time
05 mn			43'-0"	33'-0"	
10 mn			43'-1"	33'-1"	
15 mn			43'-2"	33'-2"	
20 mn			43'-3"	33'-3"	
30 mn			43'-4"	33'-4"	
40 mn			43'-5"	33'-5"	
50 mn			43'-6"	33'-6"	
60 mn			43'-7"	33'-7"	
75 mn			43'-8"	33'-8"	
90 mn			43'-9"	33'-9"	
120 mn			43'-10"	33'-10"	
150 mn			43'-11"	33'-11"	
180 mn			44'-0"	34'-0"	
210 mn			44'-1"	34'-1"	
240 mn (8 hrs)			44'-2"	34'-2"	

S SAE/SAE
Date

সে: এনাথল হক
CS-18/DA-001/11/11
১৪৪৮৬৩, ৪৬:২, আটোয়ারী জোন
আটোয়ারী, পঞ্চদুর্গ

Asstt Engr.
Date

১৪৪৮৬৩, ৪৬:২, আটোয়ারী জোন
আটোয়ারী, পঞ্চদুর্গ

K. H. ENTERPRISE

For the Contractor

Date

Proprietor



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

PUMP TEST RECORD

(Period : 1 hours)

150% Discharge

Page No: 5

Date: 5/12/2006	Well No : 10
Starting Time 15 hrs 0 minute, Capacity of Pump 5.0 cusec	District : Rajshahi
Ref. Mark (Top of Housing) 2'-0" ft. above G.L.	Upazilla : Faridpur
Static Water Level 10'-0" ft. below top of Housing Pipe	Union : Balarampur
Size of Orifice 5 inch, Size of Delivery Pipe 5 inch	Mouza : Balarampur
Length of UWC 110 ft, Depth of Pump Setting 83 ft.	J.L. No : 57
	Plot No : 5.6

Time	Piezometric Height (ft)	Discharge (cusec)	Pumping Water Level below Ref. Mark (ft.)	Actual Draw-Down (ft.)	Remarks
1	2	3	4	5	6
00mn (8hrs.)	113"	3.00	44'-2"	34'-2"	
01 mn			"	"	
02 mn			"	"	
03 mn			"	"	
04 mn			"	"	
05 mn			"	"	
06 mn			"	"	
07 mn			"	"	
09 mn			"	"	
11 mn			"	"	
13 mn			"	"	
15 mn			"	"	
20 mn			"	"	
25 mn			"	"	
30mn			44'-2"	34'-2"	
40 mn			"	"	
50 mn			"	"	
60 mn (9 hrs)			"	"	

S SAE/SAE

Date 05/12/2006

Asstt. Engr. (সহ প্রকল্প ইঞ্জিনিয়ার)

Date 05/12/2006
সহ প্রকল্প ইঞ্জিনিয়ার
আ.ডি.আর. অফিস
আ.ডি.আর. প্রকল্প

K. H. ENTERPRISE

For the Contractor

Date 05/12/2006

C-10-BMD-23-118(155) ডি.আর. অফিস
আ.ডি.আর. প্রকল্প



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAISHAH

RECOVERY RECORD

(Period : 2.5 hours)

150% Discharge

Page No.6

Date: 05/12/2006
Starting Time 16 hrs 00 minute, Capacity of Pump 2.0 cusec
Ref. Mark (Top of Housing) 2'-0" ft. above G.L.
Static Water Level 10'-0" ft. below top of Housing Pipe
Size of Orifice 6 inch, Size of Delivery Pipe 5 inch
Length of UWC 110 ft., Depth of Pump Setting 05 ft.

Well No. 101
District Rajshahi
Upazilla Barisal
Union Barisal
Mouza Barisal
T.L. No. 101
Plot No. 101

Time	Water Level below Reference Mark (ft.)	Remarks
00mn (9 hrs)	44'-2"	Pumping discontinued
02 mn	13'-6"	
04 mn	12'-11"	
06 mn	12'-4"	
08 mn	11'-11"	
10 mn	11'-5"	
15 mn	11'-2"	
20 mn	10'-10"	
25 mn	10'-7"	
30 mn	10'-5"	
40 mn	10'-4"	
50 mn	10'-3"	
60 mn	10'-2"	
75 mn	10'-1"	
90 mn	10'-1"	
105 mn	10'-1/2"	
120 mn	10'-1/2"	
135 mn	10'-0"	
150 mn (11.5 hours)	10'-0"	

S SAE/SAE

Date 05/12/2006

Asstt. Engr. (Barind Multipurpose Development Authority)

Date 05/12/2006

For the Contractor
Date 05/12/2006

CH/RA/DA2-118(P-3)



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

MULTIPLE STEP TEST
(Period : 4.5 hours)

Page No : 7

Date: 5/12/2006	Well No :
Starting Time 18 hrs 30 minute, Capacity of Pump 2.00 cusec	District : Lal nagore
Ref. Mark (Top of Housing) 2'-0" ft. above G.L.	Upazilla : Ashgari
Static Water Level 10'-0" ft. below top of Housing Pipe.	Union : Balarampur
Size of Orifice 6 inch. Size of Delivery Pipe 5 inch.	Mouza : Zalmagh
Length of UWC 110 ft. Depth of Pump Setting 33	J.E. No : 57
	Plot No : 56

Time	Piezometric Height (inch)	Discharge (cusec)	Pumping Water Level (ft.)	Actual Draw Down (ft.)	Remarks
00mn (11.5hrs)	53"	2.00	32'-2"	22'-2"	100% Discharge
10 mn			32'-3"	22'-3"	
20 mn			32'-4"	22'-4"	
30 mn			32'-5"	22'-5"	
45 mn			32'-6"	22'-6"	
60 mn			32'-7"	22'-7"	
90 mn			32'-8"	22'-8"	
100 mn	64"	2.5	36'-0"	26'-0"	125% Discharge
120 mn			38'-1"	28'-1"	
135 mn			38'-2"	28'-2"	
150 mn			38'-3"	28'-3"	
180 mn			38'-4"	28'-4"	
190 mn	113"	3.00	43'-7"	33'-7"	150% Discharge
200 mn			43'-8"	33'-8"	
210mn			43'-9"	33'-9"	
225 mn			43'-10"	33'-10"	
240 mn			43'-11"	33'-11"	
270 mn (16 hrs)			44'-0"	34'-0"	

SWL :	10'-0"	ft.
PWL :	44'-0"	ft.
Final discharge	3.00	cusec
Specific Draw Down	11.33	ft/cusec.

S SAE/SAE

Date 05/12/2006

Asstt. Engr.

Date 05/12/2006

C 10 BMD/A2-118 (P-1)

স্বাক্ষরিত হইবে, আটোরা জেলা

আটোরা জেলা, পঞ্চদশ

স্বাক্ষরিত হইবে, আটোরা জেলা

আটোরা জেলা, পঞ্চদশ

K. H ENTERPRISE

For the Contractor

Date 05/12/2006

Proprietor



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

COMPLETION CERTIFICATE OF PUMP HOUSE

Well No :
District : Baranagore
Upazilla : Autoary
Union : Balarampur
Mouza : Kalouagh
J.L. No : 57
Plot No : 516

Name of Contractor :

K. H. Enterprise,

Date of Starting : 6/12/06

Date of Completion : 5/1/07

Certified that the contractor has completed the construction work of pump house successfully at the above mentioned site as per specification in accordance with clause-18 of the general and special conditions of contract.

Following works have been completed specifically and checked the works personally:

Sl. No.	Descriptions of works	Completed (Yes/No.)	Remarks
1.	Plastering work	Yes	
2.	Slab casting	Yes	
3.	Roof casting	Yes	
4.	Discharge box		
5.	White washing	Yes	
6.	Lime tracing/Bitumin emulsion	Yes	
7.	Fitting of door made of wood/metal sheet with proper paint	Yes	
8.	Pump and Engine base	Yes	
9.	RCC beam	Yes	
10.	Ditch filling and Site development	Yes	
11.	Lock & Key supply (2 nos)	Yes	

12. 12" dia lifting hook.

SSAE/SAE
Date

Asstt Engr.
Date

K. H. ENTERPRISE
For the Contractor
Date Proprietor

C: 5-BMDA-003(P-1)

স্বঃ এনাথুল হক
উপ-সহকারী প্রকৌশলী
বিএমডিএ, বই-২, আটোরাঙ্গী জোন
আটোরাঙ্গী, পঞ্চদণ্ড।

স্বাক্ষরিত, বই-২, আটোরাঙ্গী জোন
আটোরাঙ্গী, পঞ্চদণ্ড।



**BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH**

INSPECTION OF VERTICALITY OF THE TUBEWELL

Before Pump Installation

1. Well No. :
2. District : **Ponchaigore**
3. Upazilla : **Autara**
4. Union : **Balarampur**
5. Mouza : **Kalomagi**
6. J.L. No. : **57**
7. Plot No. : **516**
8. Total Length of the Tubewell : **209'-4"**
9. Length of UWC (Excluding Reducer) **110'** ft. Date : **03/12/2006.**
10. Name of Sinking Contractor : **A. Kalam Enterprise.**

VERTICALITY DATA SHEET

Suspension Height (H) **10'** ft. Dia of UWC, d_1 **14.00** inch
Dia of Disc, d_2 **13.5** inch

Depth in ft. L	Deviation in inch X	Bearing Reading Pointing North	Calculated Deviation in inch $D' = \frac{X(L+H)}{H}$	Disc Factor $C = \frac{d_1 - d_2}{2}$	Deviation in inch $D = D' + C$
10'	0	West	0	0.25	0.75
20'	0	-	0	"	0.25
30'	1/16	-	0.25	"	0.5
40'	1/16	-	0.31	"	0.56
50'	1/16	-	0.37	"	0.62
60'	2/16	-	0.87	"	1.12
70'	2/16	-	1.00	"	1.25
80'	2/16	-	1.12	"	1.37
90'	2/16	-	1.25	"	1.5
100'	2/16	West	1.37	"	1.62
110'					
120'					

11. Maximum Deviation : **1.62** inch at depth **100'** ft.
12. Other observation, if any :
13. Straightness : Dolly passed upto **100'** ft. freely in the UWC

SSAE/SAE

Date

Asstt. Engr.

Date

K. H ENTERPRISE

For the Contractor

Date

Proprietor



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH

PUMP AND ENGINE INSTALLATION

Well No :

Name of Contractor :

District : Panchagora

Upazilla : Autoary

A. KALAM ENTERPRISE.

Union : Balarampur

Mouza : Kalomagh

J.L. No : 57

Date of Starting :

Plot No : 516

Date of Completion :

Engine Type CHINA Engine No. -

Gear Frame type GP - Gear Drive No. -

Pump Category Submersible-60' i. Pump No. -

Discharge Head No. -

No. of long column pipe 6x10' No. of short column pipe -

Length of suction pipe with bell mouth : -

Total length of pump installation 64' Length of discharge pipe 1 No.

Is the engine exhaust pipe fixed and kept out of the pump house : Yes/No.

Comments, if any :

SSAE/SAE

Date


Asstt Engr.

Date

K. H ENTERPRISE

For the Contractor

Date Proprietor



COMMISSIONING ACCEPTANCE TEST
RECORD : DURATION 6 : HRS

Date 10-9-07 Starting time 08 hr. 00 min.

... for clause of the contract?

1. Is the Exhaust pipe properly fixed & kept out of pump house as per the house (where applicable)?

2. Is the fuel tank properly fixed with the pump house?

K. H. ENTERPRISE

For the Copriagier

Ass: Engineer

SSAE/SAE

Ass: Engineer
Date.....

Date.....SSAE/SAE

বরেন্দ্র বহুমুখী উন্নয়ন কর্তৃপক্ষ

রাজশাহী।

গভীর নলকূপ হস্তান্তর ফরম

আমি B.M.D.A. প্রকল্প Porchagore Zone.
 গ্রাম Balarampur পোঃ Balarampur জেলা Porchagore
 এতদ্বারা (সমিতির নাম) Kalomagi পক্ষ হইতে দাগ নং 516
 জে. এল. নং 57 মৌজা Kalomagi উপজেলা Autogy
 জেলা Porchagore নি. এম. ডি. এ. কর্তৃক স্থাপিত গভীর নলকূপটি আনুষঙ্গিক যন্ত্রপাতিসহ চালু
 অবস্থায় অদা ২৩/১/০৭ তারিখ নি. এম. ডি. এ. এর প্রতিনিধির নিকট হইতে নলকূপ ব্যবহার
 বন্ধপাবেক্ষণ, গুপ্ত তৈরী ও যথাযথ তত্ত্বাবধানের দায়িত্ব বুঝিয়া গইলাম।

গভীর নলকূপের বিবরণ

- ১। ইঞ্জিনের/বিদ্যুতিক মটরের মডেল ও নং China.
- ২। পাম্পের গেইক ও মডেল নং Submersible 60"l.
- ৩। পিয়ার বক্স নং _____
- ৪। ডেলিভারী পাইপ 1 Nos.
- ৫। স্পাইসার স্যান্ড _____
- ৬। টুংসের বিবরণ _____

- ক) Starter.
- খ) Main Switch.
- গ) etc.
- ঘ) _____
- ঙ) _____
- চ) _____
- ছ) _____

(এই তার পুরা নাম ও ঠিকানা)

K. H ENTERPRISE

M.SN

Proprietor

১। ঠিকাদারের পক্ষে
তারিখঃ২। নি. এম. ডি. এ.র পক্ষে—
তারিখঃ
