

BM DA-04

[illegible]

SSAE/SAE

Date _____

Asstt. Engr. (Civil) (Retd.)

Date _____

K. H ENTERPRISE

For the Contractor

Date _____ Proprietor _____

উপ-সহকারী প্রকৌশলী
বিদ্যুৎ, ইলেক্ট্রনিক্স ও অটোমোবাইল ইঞ্জিন
আটোমোবাইল, পঞ্চগড়।



Project :

BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAHI

Well No. :

District : Paluchagore

Thana : Autoary

Union : Toria

Mouza : Sukhati

J.L. No. : 31

Plot No. : 3404

CONSTRUCTIONS DETAILS

Engineer :

BARIND MULTIPURPOSE
DEVELOPMENT AUTHORITY


Drilling Contractor :

KH. ENTERPRISE.

Operation	Date	Started	Date	Completed
Drilling	30/10/07	02/07 8.00 HRS	1/02/07	11-00 HRS
Casing				
Gravel Placing	-D/-	21.00 HRS	-D/-	23-00 HRS
Drilling diameter 22" / 24" / 44"				
Housing Pipe (Dia 14") mild steel				
UWC				
UWC (incl. Reducer)				
Lapping 1.5M.				
Total length [ft]		33.34M.		
L.W.C. (Dia inch) mild steel				
Depth below GL				
From.....to.....		Length [ft]		
From.....to.....		Length [ft]		
Total length [ft]				
Screen (8") inch slot, stainless steel/FG Dia 6"/8"/14"				
Depth below GL		From 32.74M to 61.90M		Length [ft]
From.....to.....		Length [ft]		
Lapping .76M.		Total length [ft]		
Total length [ft]		29.24M.		
Bailplug (Dia 11")				
Depth below GL		From 61.90 to 62.97M		
From.....to.....		Length [ft]		
Total length [ft]		.99M.		
Centralizers				
Depth below GL at				
112, 132, 152, 172, 192, 209M.				
Total Numbers		6 Nos.		
Gravel				
Gravel quantity (approx)		15.58 cum.		
Depth below GL		From GL to 220		Length [ft]
From.....to.....		Length [ft]		
Fixture length		15.58 cft.		
from top of UWC to bottom of Bail plug		63.57M.		
Verticality test				
max. deviation		1.62 inch at 100 ft		
Depth				
Date 01/02/2007.				
Material used 1/4" with Reducer 3 inch bail plug				
34.04+30.99=65.03 Lapping 1.5+1.76=3.26M.				

Cross Section of the well

(NOT TO SCALE)

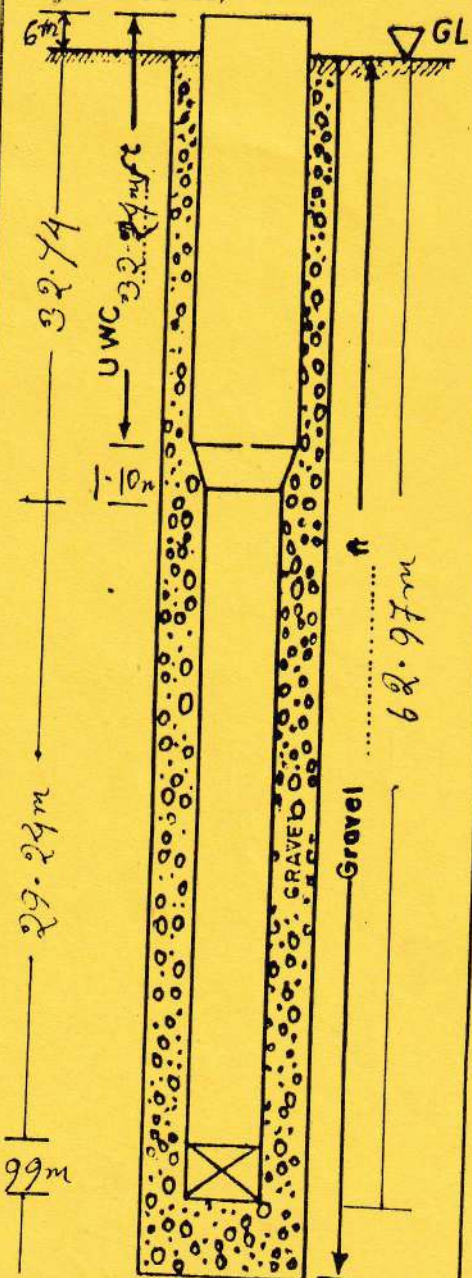Ordered depth 62.97M.
(From GL to Bottom of Bail plug)

K. H ENTERPRISE

SAE/Sr. SAE
Date 01/02/2007Asstt. Engineer
DateFor the Contractor
Date



**BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH**

INSPECTION OF VERTICALITY OF THE TUBEWELL

Before Shrouding

1. Well No. :
2. District : Panchagore
3. Upazilla : Autoary
4. Union : Toria
5. Mouza : Sukhati
6. J.L. No. : 31
7. Plot No. : 3404
8. Total Length of the Tubewell : 209' - 4"
9. Length of UWC (Excluding Reducer) 110' ft. Date : 01/07/2007
10. Name of Sinking Contractor : K. H. ENTERPRISE.

VERTICALITY DATA SHEET

Suspension Height (H) 10 ft. Dia of UWC, d_1 4" inch
Dia of Disc, d_2 3.5" inch

Depth in ft. L.	Deviation in inch X	Bearing Reading Pointing North	Calculated Deviation in inch $D' = \frac{X(L+H)}{H}$	Disc Factor $C = \frac{d_1 - d_2}{2}$	Deviation in inch $D = D' + C$
10'	0	-	-	.25	.25
20'	0	-	-	-	.25
30'	1/16	R	.25	-	.50
40'	1/16	-	.31	-	.56
50'	1/8	-	.75	-	1.00
60'	1/8	-	.87	-	1.12
70'	1/8	-	1.00	-	1.25
80'	1/8	-	1.25	-	1.37
90'	1/16	-	.62	-	.87
100'	1/16	-	.68	-	.93
110'					
120'					

11. Maximum Deviation : 1.37 inch at depth 80 ft.
12. Other observation, if any :

SSAE/SAE

Date ০১/০৭/০৭

Asstt. Engr. সহকারী প্রকৌশলী

Date ০১/০৭/০৭
পরিদর্শক, বারি ম. অ. অফিসার ১ প্রকল্প
আই.ই.এ. নং ১০৮৩

K. H. ENTERPRISE

For the Contractor

Date ০১/০৭/০৭ **Proprietor**



**BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH**

INSPECTION OF VERTICALITY OF THE TUBEWELL

After Shrouding

1. Well No. :
2. District : **Pabna**
3. Upazilla : **Autoary**
4. Union : **Toria**
5. Mouza : **Suknati**
6. J.L. No. : **3**
7. Plot No. : **3404**
8. Total Length of the Tubewell : **69'-4"**
9. Length of UWC (Excluding Reducer) **10'** ft. Date : **01/02/2007**
10. Name of Sinking Contractor : **K. H ENTERPRISE**

VERTICALITY DATA SHEET

Suspension Height (H) **10'** ft. Dia of UWC, d_1 **4"** inch
Dia of Disc, d_2 **3.5"** inch

Depth in ft. L	Deviation in inch X	Bearing Reading Pointing North	Calculated Deviation in inch $D' = \frac{X(L+H)}{H}$	Disc Factor $C = \frac{d_1 - d_2}{2}$	Deviation in inch $D = D' + C$
10'	1/16	1	.12	.5	.37
20'	1/16	-	.18	-	.43
30'	1/8		.50	-	.75
40'	1/8		.62	-	.87
50'	1/16		.37	-	.62
60'	1/16	-	.43	-	.68
70'	1/16	-	.50	-	.75
80'	1/16	-	.56	-	.81
90'	1/8	-	1.25	-	1.50
100'	1/8	1.5	1.37	-	1.62
110'					
120'					

11. Maximum Deviation : **.62** inch at depth **100'** ft.
12. Other observation, if any :
13. Straightness : Dolly passed upto **100'** ft. freely in the UWC.

K. H ENTERPRISE

SSAE/SAE

Date

Asst. Engr.

Date

For the Contractor

Date

স্বাক্ষর : এনাথুল হক
উপ-সহকারী প্রকৌশলী
জি. ২/৮৮/৮২/২১১/৮
আটোরাহা, পঞ্চদশ



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

DEVELOPMENT RECORD (Period : 2 hour)

Page No : 1

Date: 02/02/2007	Well No :
Starting Time 7 hrs 00 minute, Capacity of Pump 3 cusec	District : Panchagora
Ref. Mark (Top of Housing) 2' ft. above G.L.	Upazilla : Autoary
Static Water Level 10 ft. below top of Housing Pipe.	Union : Toria
Size of Orifice 5 inch, Size of Delivery Pipe 6 inch	Mouza : Sukhati
Length of UWC 110 ft, Depth of Pump Setting 63 ft.	J.L. No. : 31
	Plot No. : 3404

Time	Piezometric Height (inch)	Discharge (cusec)	Pumping Water Level below Reference Mark (ft.)	Actual Draw-Down (ft.)	Remarks
1	2	3	4	5	6
00mn (8 hrs)			10'-0"	S.W.L.	50% Discharge
05 mn	13.5	1.02	20'-10"	10'-10"	
10 mn			21'-1 1/2"	11'-1 1/2"	
15 mn			21'-4 1/2"	11'-4 1/2"	
20 mn			21'-6 1/2"	11'-6 1/2"	
25 mn			21'-8"	11'-8"	
30 mn			21'-9"	11'-9"	
35 mn	53	2.00	32'-1/2"	22'-1/2"	100% Discharge
40 mn			32'-3 1/2"	22'-3 1/2"	
45 mn			32'-5 1/2"	22'-5 1/2"	
50 mn			32'-7"	22'-7"	
55 mn			32'-8"	22'-8"	
60 mn			32'-9"	22'-9"	
65 mn			32'-10"	22'-10"	
70mn	84"	2.5	38'-4"	28'-4"	125% Discharge
80 mn			38'-5 1/2"	28'-5 1/2"	
90 mn			38'-6 1/2"	28'-6 1/2"	
100 mn	113"	3.00	44'-0"	34'-0"	150% Discharge
110 mn			44'-2"	34'-2"	
120 mn (2 hrs.)			44'-3"	34'-3"	

1 cusec = 28.32 LPS.

S SAE/SAE

Date ০২/০২/০৭
উপ-সহকারী প্রকৌশলী
বিদ্যুৎবিভাগ, বরিশাল জেলা
আটোরা, পঞ্চগড়।

Asstt. Engr. (বিদ্যুৎ ইন্সপেক্টর)

Date ০২/০২/০৭
সহকারী প্রকৌশলী
বিদ্যুৎবিভাগ, বরিশাল জেলা
আটোরা, পঞ্চগড়।

For the Contractor

Date ০২/০২/০৭
Proprietor

C:\10-BM\DA2-188\০২ আটোরা জেলা
আটোরা, পঞ্চগড়।



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

RECOVERY RECORD (Period : 1 hour)

Page No : 2

Date: 02/02/2007	Starting Time	9	hrs	00	Minute	Well No	
	Ref. Mark (Top of Housing)	2			ft. above G.L.	District	Rajshahi
	Static Water Level	10			ft. below top of Housing Pipe	Upazilla	Barisal
						Union	Barisal
						Mouza	Bakhat
						E.L. No	31
						Plot No	3404

Time	Water Level below Reference Mark (ft.)	Remarks
00mn		
(2 hrs)	44'-3"	
01 mn	13'-5"	
02 mn	12'-9"	
03 mn	12'-3"	
04 mn	11'-9"	
05 mn	11'-6"	
07 mn	11'-4"	
09 mn	11'-2"	
11 mn	11'-0"	
13 mn	10'-10"	
15 mn	10'-8"	
20 mn	10'-7"	
25 mn	10'-6"	
30 mn	10'-5"	
40 mn	10'-4"	
50 mn	10'-3"	
60 mn	10'-2"	
(3 hours)		

S. SAE/SAE

Date: 02/02/2007
মোঃ এনায়েত হক
উপ-সহকারী প্রকৌশলী
আবিসারী প্রকৌশলী
আবিসারী প্রকৌশলী

Asstt. Engr. (সহকারী প্রকৌশলী)
Date: 02/02/2007
আবিসারী প্রকৌশলী

K. H ENTERPRISE

For the Contractor
Date: 02/02/2007
Proprietor



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

SAND TEST RECORD (Period : 1 hour)

Page No : 3

Date: 07/02/2007	Well No
Starting Time 10 hrs. 00 minute, Capacity of Pump 3 cusec	District: Baranagore
Ref. Mark (Top of Housing) 2 ft above G.L.	Upazilla: Autoary
Static water level 10 ft below top of Housing Pipe.	Union: Toria
Size of Orifice 5 inch, Size of Delivery Pipe 6 inch	Mouza: Sukna+1
Length of UWC 10 ft, Depth of Pump setting 63 ft	J.L. No.: 31
	Plot No.: 3404

Time	Pumping Water Level below Ref. Mark (ft)	Sand Content
00mn		
(3 hrs)	40 ⁰ -2 ⁰⁰	
01 mn	42 ⁰ -10 ⁰⁰	
02 mn	42 ⁰ -2 ⁰⁰	
03 mn	42 ⁰ -2 ⁰⁰	
04 mn	42 ⁰ -4 ⁰⁰	
05 mn	42 ⁰ -6 ⁰⁰	
07 mn	42 ⁰ -7 ⁰⁰	
09 mn	42 ⁰ -9 ⁰⁰	
11 mn	42 ⁰ -11 ⁰⁰	
13 mn	43 ⁰ -1 ⁰⁰	
15 mn	43 ⁰ -3 ⁰⁰	
20 mn	43 ⁰ -5 ⁰⁰	
25 mn	43 ⁰ -12 ⁰⁰	
30 mn	43 ⁰ -9 ⁰⁰	
40 mn	43 ⁰ -10 ⁰⁰	
50 mn	43 ⁰ -11 ⁰⁰	
60 mn		
(4 hrs.)	44 ⁰ -0 ⁰⁰	

N.B.

Accepted Sand Content after 5 minutes
100 ppm and after 10 minutes-30 ppm.

Observed Result :

(a) After 5 minutes : 10 ppm
(b) After 10 minutes : 5 ppm

SSAE/SAE

Date

স্বাক্ষরিত: ০৭/০২/০৭
C-5, Barind Multipurpose Development Authority
বিদ্যমান, ৪৫১-২, আটোরা কল্যাণ
আটোরা, পঞ্চদশ

Asstt Engineer (Barind Multipurpose Development Authority)

Date

স্বাক্ষরিত: ০৭/০২/০৭
সহকারী প্রকৌশলী
বিদ্যমান, ৪৫১-২, আটোরা কল্যাণ
আটোরা, পঞ্চদশ

K. H ENTERPRISE

For the Contractor

Date

Signature



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH

Development Records
(Period : 4 hours)
150 % Discharge

Page No : 4

Date: 02/02/2007	Well No : _____
Starting Time 11 hrs 00 minute, Capacity of Pump 3 cusec	District : Panchagora
Ref. Mark (Top of Housing) 2'-0 ft above G.L.	Upazilla : Aftabgarh
Static Water Level 10 ft below top of Housing Pipe.	Union : Toria
Size of Orifice 5 inch, Size of Delivery pipe 6 inch	Mouza : Sakhati
Length of UWC 110 ft, Depth of Pump Setting 63 ft.	J.L. No : 31
	Plot No : 3404

Time	Piezometric height (ft)	Discharge (cusec)	Pumping Water Level below Ref Mark (ft)	Actual Draw-Down (ft)	Remarks
1	2	3	4	5	6
00mn (4 hrs)	113"	3.00	43'-0"	34'-0"	Back Wash only one time
05 mn			43'-11"	31'-11"	After 5mn. back wash has been taken.
10 mn			42'-2"	32'-11"	
15 mn			42'-4"	32'-4"	
20 mn			42'-6"	32'-6"	
30 mn			42'-8"	32'-8"	
40 mn			42'-10"	32'-10"	
50 mn			42'-12"	32'-12"	
60 mn			43'-3"	33'-3"	
75 mn			43'-5"	33'-5"	
90 mn			43'-7"	33'-7"	
120 mn			43'-9"	33'-9"	
150 mn			43'-11"	33'-11"	
180 mn			44'-0"	34'-0"	
210 mn			44'-1"	34'-1"	
240 mn (8 hrs)			44'-2"	34'-2"	

K. H ENTERPRISE

S SAE/SAE

Date

স্বাক্ষরিত

স্বাক্ষরিত

স্বাক্ষরিত

Asstt Engineer

Date

স্বাক্ষরিত

For the Contractor

Date

Proprietor



**BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSHAH**

PUMP TEST RECORD

(Period : 1 hour)
150% Discharge

Page No: 5

Date: 02/02/2007		Well No :	
Starting Time 15 hrs 00 minute, Capacity of Pump 3.00 cusec		District :	Rajshahi
Ref. Mark (Top of Housing) 2'-0" ft. above G.L.		Upazilla :	Autoary
Static Water Level 10'-0" ft. below top of Housing Pipe		Union :	Toria
Size of Orifice 5 inch, Size of Delivery Pipe 6 inch		Monza :	Sukna+1
Length of UWC 110 ft, Depth of Pump Setting 63 ft.		J.L. No :	31
		Plot No :	3404

Time 1	Piezometric Height (ft) 2	Discharge (cusec) 3	Pumping Water Level below Ref. Mark (ft.) 4	Actual Draw Down (ft.) 5	Remarks 6
00 min (8 hrs.)	113"	3.00	41'-2"	34'-2"	
01 min					
02 min					
03 min					
04 min					
05 min					
06 min					
07 min					
09 min					
11 min					
13 min					
15 min					
20 min					
25 min					
30 min			44'-2½"	34'-2½"	
40 min			"	"	
50 min			"	"	
60 min (9 hrs)			44'-3"	34'-3"	

S.SAE/SAE

Date ০২/০২/২০০৭

উপ-সহকারী প্রকৌশলী
বিদ্যুৎ ও ইঞ্জিনিয়ারিং বিভাগ
আইসিডিআর

Asstt. Engr

Date ০২/০২/২০০৭
সহকারী প্রকৌশলী
বিদ্যুৎ ও ইঞ্জিনিয়ারিং বিভাগ
আইসিডিআর

K. H ENTERPRISE

For the Contractor

Date Proprietor



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAH

RECOVERY RECORD

(Period : 2.5 hours)

150% Discharge

Page No:6

Date: 02/02/2007	Well No
Starting Time 16 hrs 00 minute, Capacity of Pump 3 cusec	District: Faichagore
Ref. Mark (Top of Housing) 2 ft. above G.L.	Upazilla: Autoary
Static Water Level 10 ft. below top of Housing Pipe.	Union: Toria
Size of Orifice 5 inch, Size of Delivery Pipe 6 inch	Mouza: Sukhati
Length of UWC 110 ft., Depth of Pump Setting 63 ft.	J.L. No: 31
	Plot No: 3404

Time	Water Level below Reference Mark (ft.)	Remarks
00mn (9 hrs)	44'-3"	Pumping discontinued
02 mn	12'-6"	
04 mn	11'-6"	
06 mn	11'-3"	
08 mn	11'-1 1/2"	
10 mn	11'-0"	
15 mn	10'-6"	
20 mn	10'-5"	
25 mn	10'-3"	
30 mn	10'-2"	
40 mn	10'-1 1/2"	
50 mn	10'-1"	
60 mn	10'-1/2"	
75 mn	10'-1/2"	
90 mn	10'-1/2"	
105 mn	10'-1/2"	
120 mn	10'-1/2"	
135 mn	10'-0"	
150 mn (11.5 hours)	10'-0"	

S SAE/SAE

Date ০২: ০২/০২/০৭

C-10-BMDA2-118(P-3)

Asstt. Engr (মোঃ নজিবুল ইসলাম)
Date ০২/০২/০৭

For the Contractor
Date ০২/০২/০৭

Proprietor



MULTIPLE STEP TEST
(Period : 4.5 hours)

Page No : 7

Date: 02/02/2007

Starting Time 18 hrs 30 minute, Capacity of Pump 3 cusec

Ref. Mark (Top of Housing) $2'-0"$ ft. above G.L.

Static Water Level 10'-0" ft. below top of Housing Pipe.

Size of Orifice 5 inch, Size of Delivery Pipe 6 inch

Length of UWC 110 ft. Depth of Pump Setting 63

Well No

District : **Panchagore**

Upazilla : Aurang

Union : Toria

Mouza : Suknati

J. I. No - 31

Plot No 3404

Time	Piezometric Height (inch)	Discharge (cusec)	Pumping Water Level (ft.)	Actual Draw Down (ft.)	Remarks
1	2	3	4	5	6
00mn (11.5hrs)	-	-	10'-0"	S.W.L.	100% Discharge
10 mn	53"	2.00	32'-0"	22'-0"	
20 mn			32'-3"	22'-3"	
30 mn			32'-6"	22'-6"	
45 mn			32'-8"	22'-8"	
60 mn			32'-9"	22'-9"	
90 mn			32'-9 1/2"	22'-9 1/2"	
100 mn	84	2.5	38'-1/2"	28'-1/2"	125% Discharge
120 mn			38'-2 1/2"	28'-2 1/2"	
135 mn			38'-4"	28'-4"	
150 mn			38'-5"	28'-5"	
180 mn			38'-5 3/4"	28'-5 3/4"	
190 mn	113"	3.00	43'-7"	33'-7"	150% Discharge
200 mn			43'-9"	33'-9"	
210mn			43'-11"	33'-11"	
225 mn			44'-1/2"	34'-1/2"	
240 mn			44'-1 1/2"	34'-1 1/2"	
270 mn (16 hrs)			44'-2"	34'-2"	

SWI : $10^0 - 10^9$

PWL: 44°-2"

Final discharge	3.00
-----------------	------

Specific Draw Down 11.30ft./

i

仇

cusec

fi/ensee

K. H ENTERPRISE

S SAE/SAE

Date: ১০/০৫/২০২০

Asstt. Engr. *कविशंकर शिवाजी*

Date _____

For the Contractor

Date _____ Proprietor _____

আটোরাড়ী, পঞ্চসভা।

BAIRABDI MULTIPURPOSE DEVELOPMENT AUTHORITY RAJSHAHI

COMPLETION CERTIFICATE OF PUMP HOUSE

Well No : _____ District : **Panchagore** Upazilla : **Autary** Union : **Torla** Mouza : **Sukhant** JL No : **31** Plot No : **3404**

Name of Contractor : _____

Date of Starting : **3/2/2007** Date of Completion : **3/3/2007**

KH. ENTERPRISE.

Certified that the contractor has completed the construction work of pump house successfully at the above mentioned site as per specification in accordance with clause-18 of the general and special conditions of contract.

Following works have been completed specifically and checked the works personally: -

Sl. No.	Descriptions of works	(completed (Yes/No.)	Remarks
1.	Plastering work	Yes	
2.	Slab casting	Yes	
3.	Roof casting	Yes	
4.	Discharge box	-	
5.	White washing	Yes	
6.	Lime tracing/Bitumin emulsion	Yes	
7.	Filling of door made of wood/metal	Yes	
	sheet with proper paint	Yes	
8.	Pump and Engine base	Yes	
9.	RCC beam	Yes	
10.	Ditch filling and Site development	Yes	
11.	Lock & Key supply (2 nos)	Yes	

SSA/SAFE

Date

Asstt. Lgr.

Date

KH. ENTERPRISE

Date

Proprietor



BARIND MULTIPURPOSE DEVELOPMENT AUTHORITY
RAJSTHAN

INSPECTION OF VERTICALITY OF THE TUBEWELL

Before Pump Installation

- Well No. : 3404
- District : Panchsagar
- Upazilla : Autary
- Union : Torla
- Alouza : Suknati
- Plot No. : 31
- Total Length of the Tubewell : 209'-4"
- Length of UWC (Excluding Reducer)
- Name of Sinking Contractor : K.M. ENTPRPRISE.

23.7.07
Date : 07/02/2007.


VERTICALITY DATA SHEET

Suspension Height (H) 10 ft
Dia of UWC, d₁ 14"
Dia of Disc, d₂ 13.5"
inch

Depth in ft.	Deviation in inch X	Bearing Pointing North	Calculated Deviation in inch X (d ₁ /H)	Disc Factor C = d ₁ /d ₂	Deviation in inch D = D ₁ C
19'	1/16	NE	.12	.25	.37
29'	1/16	-	.18	-	.43
30'	1/8	-	.50	-	.75
40'	1/8	-	.62	-	.87
50'	1/16	-	.37	-	.62
60'	1/16	-	.43	-	.68
70'	1/16	-	.50	-	.75
80'	1/16	-	.56	-	.81
90'	1/8	-	1.25	-	1.50
100'	1/8	NE	1.37	-	1.62
110'					
120'					

- Maximum Deviation : 1.62
- Other observation, if any :
- Straightness : Bolly passed upto 100 ft. freely in the UWC

SSA/SAE
Date : 07/02/2007
Asst. Engineer (Civil)
For the Contractor
Date : 07/02/2007
Barind Multipurpose Development Authority
Rajasthan




KL. ENTERTAINING.

Date of Starting : 23.7.07
Date of Completion : 23.7.07

Postmaster
Address
Only
Sukma 41

[illegible]

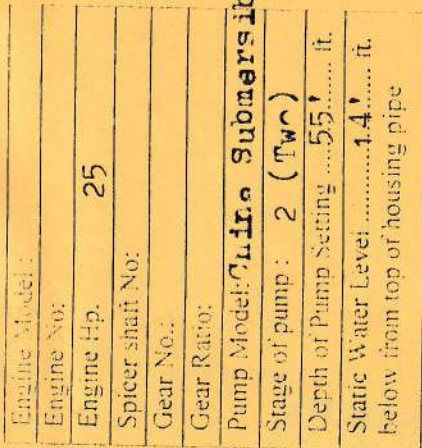

BARING MULTIPURPOSE DEVELOPMENT AUTHORITY

RAJSHAHII

COMMISSIONING/AcCEPTANCE TEST

RECORD : DURATION 6 : HRS

Cell No	:	
District	:	Pondicherry
Upazilla	:	Antony
Union	:	Toria
Mouza	:	Sukhathi
J.L. No	:	31
Plot No	:	3404
Date	14.09.08	
Starting time	08	hr 00 min

Hrs. Run	Time Hour Meter Reading	R.P.M.	Oil press.	Engine temp. °C	Dis- charge, cu. sec.	Fuel consumption Litre					Litres per hp-hr = $\frac{\text{Litre}}{\text{hp-hr}}$	Pumping Water Level, ft.	Specific Drawdown, ft. cu. sec.	Remarks	
						Start	stop	Fuel Used	Start	stop					Min.
1	2	5	4	5	0	3	0	10	11	12	13	14	15	16	
0 hr.	00017					00017									
1 hr.					2		22	5.00		60	.23		14'-0"	3.4 I.	
2 hr.					"		"			"			36'-2 $\frac{1}{2}$ "		
3 hr.					"		"			"			36'-3"		
4 hr.					"		"			"			36'-4 $\frac{1}{2}$ "		
5 hr.					"		"			"			36'-5 $\frac{1}{2}$ "		
6 hr.	00149				"		"			"			36'-5 $\frac{1}{2}$ "		
					"	00149	"		14.00				36'-6 $\frac{1}{2}$ "	17.30 ft/cu. sec.	

used no other
LH Enricher
prepaid method

SAE/SAE

Date 24/10/07

C.10-BMDA2-120

উপ-মহক।বী প্রকৌণবী

শিওমস্টিং, ইউ-২, অটোমারী স্টোয়া

For the Contractor

Date _____

AN INTERPRETATION

五

✓ **Investment**

1. Is the exhaust pipe properly fixed & kept out of pump house as per clause of the contract?
2. Is the fuel tank properly fixed with the pump house (where applicable)?
3. Is the Tubewell reference plaque fixed in the pump house?

100

अइक। *Ma*

১৫. হুউনিট-২, আভোমারী জেল

ଆଜ୍ଞାପାତ୍ରୀ, ମହମ୍ମଦ ।

