

## বাংলাদেশ হাই-টেক পার্ক কর্তৃপক্ষের ইনোভেশন

**১.০) সেবার নামঃ** IoT based Project Management and Digital Project Tracking System.

**উদ্ভাবকঃ** জনাব মোহাম্মদ আতিকুল ইসলাম, উপ-পরিচালক (পরিকল্পনা)  
বাংলাদেশ হাই-টেক পার্ক কর্তৃপক্ষ।

**উপদেষ্টাঃ** জনাব জনাব সৈয়দ জহুরুল ইসলাম (যুগ্মসচিব)  
পরিচালক (কারিগরি),(অতিরিক্ত দায়িত্ব)  
বাংলাদেশ হাই-টেক পার্ক কর্তৃপক্ষ।

**সদস্যঃ** জনাব হাসান মারুফ পারভেজ, উপ-প্রকল্প পরিচালক  
বঙ্গবন্ধু হাই-টেক সিটি-২ এর সহায়ক অবকাঠামো নির্মাণ প্রকল্প।  
জনাব মোঃ সাজ্জাদ হোসেন , উপ-সহকারী প্রকৌশলী (ই/এম)  
বঙ্গবন্ধু হাই-টেক সিটি-২ এর সহায়ক অবকাঠামো নির্মাণ প্রকল্প।

### ১.১) প্রেক্ষাপটঃ

ডিজিটাল বাংলাদেশ বিনির্মাণে বাংলাদেশ হাই-টেক পার্ক কর্তৃপক্ষ দেশের বিভিন্ন স্থানে হাই টেক পার্ক, সফটওয়্যার টেকনোলজি পার্ক, আইটি পার্ক, আইটি ভিলেজ, আইটি হাব প্রতিষ্ঠা করার জন্য বিভিন্ন প্রকল্প গ্রহণ করেছে। এ সকল প্রকল্পের কাজসমূহ বাস্তবায়নের জন্য বিভিন্ন সময় বিভিন্ন সমস্যার সম্মুখীন হতে হয়।

- প্রকল্পের বিভিন্ন কাজের সিদ্ধান্ত গ্রহণের দীর্ঘতা;
- সার্বক্ষণিক প্রকল্পের কাজ তাদারকি করতে না পারা;
- কোভিড-১৯ ও অন্যান্য প্রাকৃতিক দুর্যোগ;
- প্রকল্প অফিস হতে প্রকল্প এলাকায় যাতায়াত;

### ১.২) IoT based Project Management and Digital Project Tracking System উদ্ভাবনী উদ্যোগ গ্রহণের যৌক্তিকতাঃ

IoT based Project Management and Digital Project Tracking System সফটওয়্যারটির মাধ্যমে নির্মাণাধীন বিভিন্ন হাই-টেক পার্কসমূহে প্রকল্পগুলোকে একটি মাত্র প্ল্যাটফর্মে সহজেই মনিটরিং, সুপারভিশন করা সহজীকরণ হবে;

- অদক্ষ সংস্থান এবং আর্থিক পরিকল্পনা হ্রাস হবে;
- প্রকল্প এলাকা ঠিকাদারি প্রতিষ্ঠানের সময় এবং দীর্ঘসূত্রতা হ্রাস পাবে;
- ডিজিটাল বাংলাদেশ বিনির্মাণে সহায়ক ভূমিকা পালন করবে;
- ঠিকাদারি প্রতিষ্ঠানের কার্যক্রম ট্র্যাকিং করা;
- সকল ঠিকাদারি প্রতিষ্ঠানকে একটি প্ল্যাটফর্মে অন্তর্ভুক্ত করা ;
- অপ্রয়োজনীয় সময়সীমা বৃদ্ধির সুযোগ কমিয়ে দেয় ;

### ১.৩) প্রস্তাবিত/বাস্তবায়িত ইনোভেশনের বর্ণনাঃ

আইওটি-ভিত্তিক ডিজিটাল প্রকল্প ট্র্যাকিং সিস্টেম ("আইওটি-ভিত্তিক ডিপিটিএস") এমন একটি সিস্টেম যা কোনও প্রকল্পকে দূর থেকে পর্যবেক্ষণ করা যায়। প্রাথমিকভাবে এই সফটওয়্যারটিতে প্রকল্পের সমস্ত তথ্য ইনপুট হবে এবং প্রতিদিনের কাজের অগ্রগতি, চ্যালেঞ্জ ইত্যাদি হালনাগাত করা হবে। এই সিস্টেমে একটি কেন্দ্রীয় ড্যাশবোর্ড বা কাজের আপডেট প্যানেল ব্যবহার করে প্রকল্পের সামগ্রিক কার্যক্রম যেমনঃ Daily Work Update Report, Package Summary Report, Company Details Report, Package Wise Item Report দেখা যাবে।

System Modules	
<b>Admin</b> <ul style="list-style-type: none"><li>▪ Menu</li><li>▪ Dashboard</li></ul>	
	



## Reporting

- Daily Work Update Report
- Package Summary Report
- Company Details Report
- Package Wise Item Report

### Package Summary Report

Land Development

Assigned Company Name	Start Date	End Date	Est. Budget	F
Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV	2020-01-08	2021-07-17	255977428.74	25

#### Packages Info

Package Name	Total Item	Items Completed	Percentage of Completed	Mobilize Amount	Paid Amount	D
Land Development	22	0	0.00%	25597742.87	0	230379685.5

#### Bill Info

Bill Id	Bill Date	Item Name	Quantity	Unit Price	To
Total					

### Company Details Report

Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV

Name	Code	Contact Person	Email	Phone
Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV	05-51567	Motlil Holader	dhakaepc@gmail.com	01709698364

#### Packages Name

Package Name	Total Item	Items Completed	Percentage of Completed	Mobilize Amount	Paid Amount	D
Land Development	22	0	0.00%	25597742.87	0	230379685.87

#### Bill Info

Land Development

Bill Id	Bill Date	Item Name	Quantity	Unit Price	To
Total					

### Package Wise Item Report

Land Development

Item Name	Percentage of Complete	Start Date	End Date	Estimated Budget	Completion Cost
3-0-20-EMP ACTIVITIES -				0.00	0.00
3-0-19-EMP ACTIVITIES -				0.00	0.00
3-0-18-EMP ACTIVITIES -				0.00	0.00
3-0-17-EMP ACTIVITIES -				0.00	0.00
3-0-16-EMP ACTIVITIES -				0.00	0.00
3-0-15-EMP ACTIVITIES -				0.00	0.00
3-0-14-EMP ACTIVITIES -				0.00	0.00
3-0-13-EMP ACTIVITIES -				0.00	0.00
3-0-12-As Built Drawing -				0.00	0.00
3-0-11-Material Test -				0.00	0.00
3-0-10-Material Test -				0.00	0.00
3-0-9-civil -				0.00	0.00
3-0-8-civil -				0.00	0.00
3-0-7-civil -				0.00	0.00
3-0-6-civil -				0.00	0.00
3-0-5-civil -				0.00	0.00

# Attendance Management

# User Attendance

App / Add User

**First Name**

**Last Name**

**Email**

**Password**

**Confirm Password**

**Company**

**User Role**

Submit

App / User List

+ Add

User List

Name	Email	Action
Md Sazzad Hossain	hsazzad968@admin.com	View Details
M/S/M N Huda Limited	mnhuda@admin.com	View Details

Showing 1 to 2 of 2 entries

Show 2 entries 1

App / Manual Attendance

**Employee Name**

**Employee ID**

**Event Type**

**Company**

**Entry Date**

**Entry Time**

Submit

**Quantity**

Submit

# User Profiles

## Employee Profile Sub-Contactor Profile

App / Add Company

1 Company Details

Company Name

No. of Employee

Email

Fax

Address

State / District

Profile image

Next

2 Administrator Details

Company Code

Contact Person

Phone

Company Type

City

Zip

App / Manage Company

Company List

Search Name...

Company Logo	Company Name	Company Email	Company Type	Working Status	Address	City	Action
	Super Admin	administrator@admin.com	Super Admin	active	Dhaka	Dhaka	Action
	Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV	dhakaepc@gmail.com	Development Partner	active	House:426 Road No.30 Mohakhali DOHS,Dhaka	Dhaka	Show Details User List Edit Delete
	Basic Infrastructure for Bangabandhu Hi-Tech City-2.Project	pdhbc97@gmail.com	Project Authority	active	Bangladesh Hi-Tech Park Authority Information & Communication Technology Division ICT Tower, Agargaon	Dhaka	Action
	Adex Corporation Limited	mahmud@adexbd.com	Development Partner	active	56, Purana Paltan	Dhaka	Action
	ATHMHE (JV)	khalurbabu1062@gmail.com	Development Partner	active	855, Shewrapara, Mirpur	Dhaka	Action
	Hi-Tech Park Development	baharhitech2@admin.com	Development Partner	active	Dhaka	Dhaka	Action
	ARMA ELECTRIC COMPANY	amra@admin.com	Development Partner	active	Dhaka	Dhaka	Action
	VITTI STHAPATI BRINDO LTD.	vittibd@gmail.com	Technical Advisor	active	27/1 SHANGSHAD AVENUE, MONIPURIPARA	Dhaka	Action
	Nationtech-Ranabuilders	nationtech@admin.com	Development Partner	active	Dhaka	Dhaka	Action
	M/S. MNHCLHMHE (JV)	mnhcl@admin.com	Development Partner	active	Dhaka	Dhaka	Action

App / Profile



**Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV**

[Message](#)

---

**Contact Information**

Email: dhakaepc@gmail.com

**Info** | Users | Packages

- Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV
  - Development Partner
  - Email: dhakaepc@gmail.com
  - Phone: 01709698364

App / Profile



**Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV**

[Message](#)

---

**Contact Information**

Email: dhakaepc@gmail.com

**Info** | **Users** | Packages

- Motilal Haolader
  - Development Partner
  - Email: MotilalHaolader@admin.com
- Toma User
  - Development Partner
  - Email: toma@toma.com

App / Profile



**Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV**

[Message](#)

---

**Contact Information**

Email: dhakaepc@gmail.com

**Info** | Users | **Packages**

- Land Development
  - Status: active
  - Start Date: 2020-01-08
  - End Date: 2021-07-17
  - Progress: 0 %

## Edit Company

**Company Name**

**No. of Employee**

**Contact Person**

**Email**

**Phone**

**Company Type**

**Address**

**City**

**State / District**

**Profile Image**

 No file chosen



## Management

- Project Package Registration
  - Package Budget Management
  - Contactors Management
  - Package Registration
  - Package Task
  - Budget & Work Approval
  - Meeting schedule
  - Construction & upload material
  - Contractor Payment Module
  - Daily work update
- Project Package Registration

### Package Registration

**Package Name**  
Package Name

**Package Number**  
Package Number

**Start Date**  
Start Date

**End Date**  
End Date

**Estimated Price**  
Estimated Price

**Final Price**  
Final Price

**Package Type**  
Package Type

**Has package lot?**  
 Yes

**Description**  
Paragraph

**Package Files**  
Drop files here or click to upload.

[Submit](#)

[+ Create Package](#) [All](#) [Ongoing](#) [Finished](#)

<p><b>WORK</b></p> <p>Land Development</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - Tomu construction &amp; Co. Ltd-Ohaka EPC company Ltd.-JV</p> <p>Jan 8, 2020 Jul 17, 2021 Progress: 0%</p>	<p><b>ELECTRICAL</b></p> <p>HT Cable</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - ARMA ELECTRIC COMPANY</p> <p>Oct 11, 2020 Mar 14, 2021 Progress: 0%</p>	<p><b>CIVIL WORK</b></p> <p>Construction of Compound Drain Utility Duct and Footpath</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - AT-HMHE (JV)</p> <p>Feb 20, 2020 Sep 23, 2021 Progress: 0%</p>
<p><b>CIVIL WORK &amp; ELECTRICAL</b></p> <p>Sub-Station</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - Adex Corporation Limited</p> <p>Jun 25, 2020 Dec 5, 2021 Progress: 0%</p>	<p><b>CIVIL WORK</b></p> <p>Construction of Internal Bituminus Carpeting Road</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - Nationtech-Ranabuilders</p> <p>Feb 13, 2020 Aug 23, 2021 Progress: 0%</p>	<p><b>CIVIL WORK &amp; ELECTRICAL</b></p> <p>Construction of SHEBA BHABAN (level 3 - level 8)</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - M/S. MNHCL-HMHE (JV)</p> <p>Apr 16, 2020 Sep 23, 2021 Progress: 0%</p>
<p><b>LOT</b></p> <p>Construction of Boundary and Sound Protection Wall</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - M/S. M N Huda Construction</p> <p>Sep 20, 2020 Aug 3, 2021 Progress: 0%</p>	<p><b>LOT</b></p> <p>Construction of 10 Storied Dormitory Building</p> <p><b>Consultant</b> - VITTI STHAPATI BRINDO LTD. <b>Development Partner</b> - M. Jamal &amp; Company Limited-Hossain Constructions (Pvt.)Ltd.-JV</p> <p>Dec 22, 2020 Nov 10, 2022 Progress: 0%</p>	

Show 2 entries

### App / Package Assign

**Select Package**

Land Development

**Select Development Partner**

Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV - (Development Partner)

**Mobilization Bill Amount**

Mobilization Bill Amount

[Submit](#)

[+ Create Package](#)
All
Ongoing
Finished

WORK	CONSULTANT	DEVELOPMENT PARTNER	START DATE	END DATE	PROGRESS
Land Development	VITTI STHAPATI BRINDO LTD.	Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV	Jan 8, 2020	Jul 17, 2021	Progress: 0%
ELECTRICAL	VITTI STHAPATI BRINDO LTD.	ARMA ELECTRIC COMPANY	Oct 11, 2020	Mar 14, 2021	Progress: 0%
CIVIL WORK	VITTI STHAPATI BRINDO LTD.	ATHMHE (JV)	Feb 20, 2020	Sep 23, 2021	Progress: 0%
CIVIL WORK & ELECTRICAL	VITTI STHAPATI BRINDO LTD.	Adex Corporation Limited	Jun 25, 2020	Dec 5, 2021	Progress: 0%
CIVIL WORK	VITTI STHAPATI BRINDO LTD.	Nationtech-Ranabuilders	Feb 13, 2020	Aug 23, 2021	Progress: 0%
CIVIL WORK & ELECTRICAL	VITTI STHAPATI BRINDO LTD.	M/S. MNHCL-HMHE (JV)	Apr 16, 2020	Sep 23, 2021	Progress: 0%
LOT	VITTI STHAPATI BRINDO LTD.	M/S. M N Huda Construction	Sep 20, 2020	Aug 3, 2021	Progress: 0%
LOT	VITTI STHAPATI BRINDO LTD.	M. Jamal & Company Limited-Hossain Construction Ltd.-JV	Dec 22, 2020	Nov 10, 2022	Progress: 0%

Show 5 entries

### DIGITAL PROJECT TRACKING SYSTEMS

**Assign Development Partner**

**Select Package**

Construction of Boundary and Sound Protection Wall

**Select Development Partner**

Mobilization Bill Amount

Mobilization Bill Amount

[Submit](#)

WORK	CONSULTANT	DEVELOPMENT PARTNER	START DATE	END DATE	PROGRESS
Land Development	VITTI STHAPATI BRINDO LTD.	Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV	Jan 8, 2020	Jul 17, 2021	Progress: 0%
CIVIL WORK & ELECTRICAL	VITTI STHAPATI BRINDO LTD.	Adex Corporation Limited	Jun 25, 2020	Dec 5, 2021	Progress: 0%
LOT	VITTI STHAPATI BRINDO LTD.	M/S. M N Huda Construction	Sep 20, 2020	Aug 3, 2021	Progress: 0%

Package: Land Development Edit Package Com

Completed 0% Status: Active

**Package Overview**

[About](#)
[Item List](#)
[Today's Update](#)
[Material List](#)
[Received Material List](#)
[Payment History](#)

[Add or Update Development Partner](#)

ক) কালিয়াটেকরহ বঙ্গবন্ধু হাই-টেক সিটি-২ এর জমিতে হাই-টেক শিল্প গড়ে তোলার লক্ষ্যে সহায়ক প্রাথমিক অবকাঠামো যেমন অভ্যন্তরীণ রাস্তা, ভূমি উন্নয়ন, বিদ্যুৎ, ইন্টারনেট এবং গ্যাস সংযোগ ইত্যাদি অবকাঠামো নির্মাণ;

খ) দেশি/বিদেশী প্রতিষ্ঠানকে বিনিয়োগে আকৃষ্ট করা; এবং

গ) কর্মসংস্থানের সুযোগ সৃষ্টি।

Start Date	End Date	Contract Price	Final Price	Mobilization Bill Amount
2020-01-08	2021-07-17	255977428.74	255977428.74	25597742.87

[Discussions](#)
[Files/Resources](#)

Your comment...

[Submit](#)

**All Activity**
[Assigned Companies](#)

Filter Activity List

All

- 3-0-1-civil -- active
- 3-0-2-civil -- active
- 3-0-3-civil -- active
- 3-0-4-civil -- active
- 3-0-5-civil -- active
- 3-0-6-civil -- active
- 3-0-7-civil -- active

### Edit Package

**Package Name** 
**Package Number**

**Start Date** 
**End Date**

**Contract Price** 
**Final Price**

**Package Type** 
**Has package lot?**  Yes

**Description**

Paragraph

**B** *I*

ক) কালিয়াটেকরহ বঙ্গবন্ধু হাই-টেক সিটি-২ এর জমিতে হাই-টেক শিল্প গড়ে তোলার লক্ষ্যে সহায়ক প্রাথমিক অবকাঠামো যেমন অভ্যন্তরীণ রাস্তা, ভূমি উন্নয়ন, বিদ্যুৎ, ইন্টারনেট এবং গ্যাস সংযোগ ইত্যাদি অবকাঠামো নির্মাণ;

খ) দেশি/বিদেশী প্রতিষ্ঠানকে বিনিয়োগে আকৃষ্ট করা; এবং

গ) কর্মসংস্থানের সুযোগ সৃষ্টি।

[Submit](#)
[Close](#)

App / Bill Management

Bill Management

Land Development

Select	Item No.	Item Name	Group	Unit	Unit Price	Quantity	Received Quantity	Due Quantity	Total	Received	Due
<input type="checkbox"/>	1	3-0-1-civil -	civil	Each	542699.10	1.00	0	1.00	0.00	0	0
<input type="checkbox"/>	2	3-0-2-civil -	civil	Sqm	2403.00	24.00	0	24.00	0.00	0	0
<input type="checkbox"/>	3	3-0-3-civil -	civil	Sqm	21.60	367438.00	0	367438.00	0.00	0	0
<input type="checkbox"/>	4	3-0-4-civil -	civil	Sqm	152.10	178361.00	0	178361.00	0.00	0	0
<input type="checkbox"/>	5	3-0-5-civil -	civil	CUM	170.10	114715.00	0	114715.00	0.00	0	0
<input type="checkbox"/>	6	3-0-6-civil -	civil	CUM	217.30	114715.00	0	114715.00	0.00	0	0
<input type="checkbox"/>	7	3-0-7-civil -	civil	CUM	271.80	257235.00	0	257235.00	0.00	0	0
<input type="checkbox"/>	8	3-0-8-civil -	civil	CUM	376.20	68738.00	0	68738.00	0.00	0	0
<input type="checkbox"/>	9	3-0-9-civil -	civil	CUM	254.00	303212.00	0	303212.00	0.00	0	0
<input type="checkbox"/>	10	3-0-10-Material Test -	Material Test	Each	2000.00	200.00	0	200.00	0.00	0	0

Show 10 entries

App / Meeting Create

Meeting Name

Date & Time

Meeting Location

Add Guest

Description

Meeting Minutes

Submit

App / IOT Device Management

IoT Device List

First Name	Last Name	Email	Company	IMEI No.	Action
Motlal	Haclader	Motlialhaclader@admin.com	Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV		
Adex	Corporation	adexcorporation@admin.com	Adex Corporation Limited		
AT	HMHE	atmhe@admin.com	AT-HMHE (JV)		
Naim	Hi-Tech	naimhitech2@admin.com	Hi-Tech Park Development	860363044704303	
Bahar	Hi-Tech 2	baharhitech2@admin.com	Hi-Tech Park Development	860363044592567	
Amra	Admin	amra@admin.com	ARMA ELECTRIC COMPANY		
Toma	User	toma@toma.com	Toma construction & Co. Ltd-Dhaka EPC company Ltd.-JV	860363044704303	
Nationtech	Admin	nationtech@admin.com	Nationtech-Ranabuilders		
Mnhcl	Admin	mnhcl@admin.com	M/S. MNHCLHMHE (JV)		
M JAMAL &	Hossain Constructin	hcpj@admin.com	M Jamal & Company Limited-Hossain Constructions (Pvt.)Ltd.-JV		

Show 10 entries

App / IOT Device & APP Registration

Device Name

IMEI No.

Email


Phone

Assignee User

Company

Submit

IoT Device List    Device Discovering



### App / Live Project Monitoring Channel

End Call



You



Remote Area



## Mobile Apps

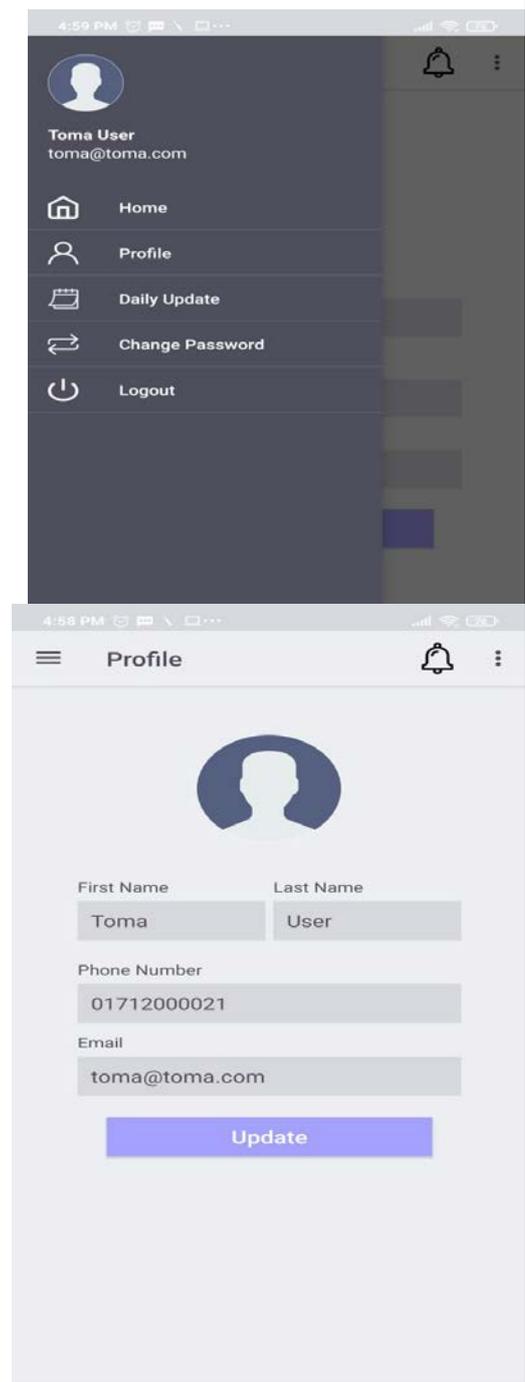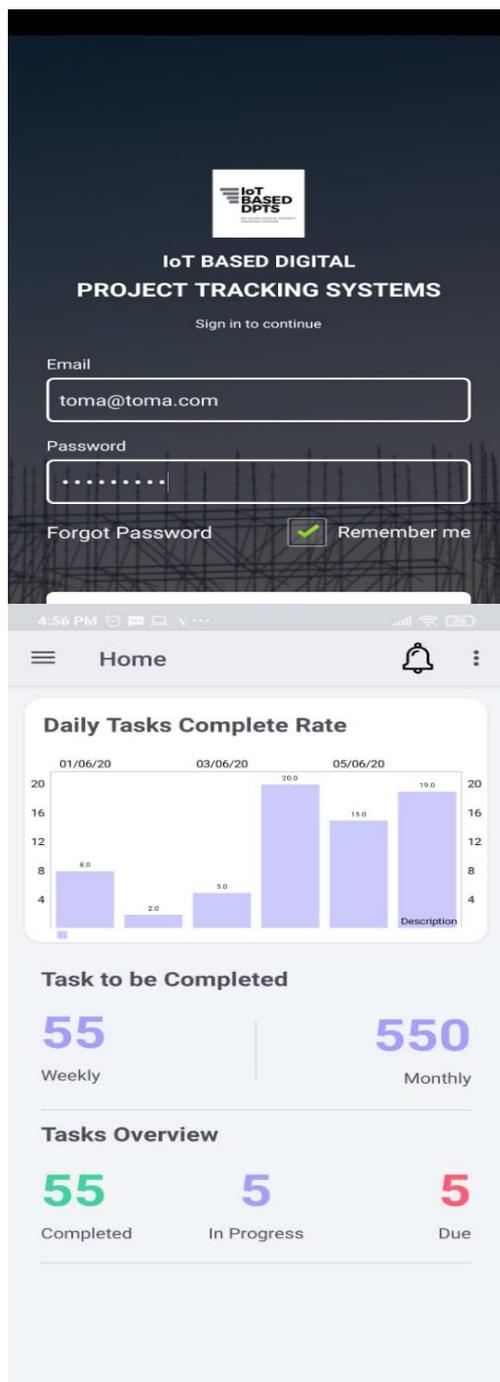

১.৪) তুলনামূলক বিশ্লেষণ(বিদ্যমান ও প্রস্তাবিত পদ্ধতি):	
বিদ্যমান পদ্ধতির বর্ণনা	প্রস্তাবিত পদ্ধতির বর্ণনা
বিদ্যমান প্রকল্পগুলোর পরিচালনা সিস্টেমটি মূলত ন্যূনতম অটোমেশন বা অপারেশন পর্যবেক্ষণ বা পরিচালনার ম্যানুয়্যাল রেকর্ডের উপর নির্ভর করে।	আইওটি-ভিত্তিক ডিপিটিএস প্রকল্প ম্যানেজমেন্টের সমালোচনামূলক বৈশিষ্ট্যগুলি সহ ডিজিটালাইজ করে: প্যাকেজ পরিচালনা <ul style="list-style-type: none"> <li>➤ অনুমোদনের ব্যবস্থাপনা</li> <li>➤ রিপোর্টিং</li> <li>➤ এইচআর পরিচালনা</li> </ul>

১.৫) প্রত্যাশিত ফলাফল TCV (Time, Cost & Visit) অনুসারে বিদ্যমান ও প্রস্তাবিত পদ্ধতির তুলনাঃ

	বিদ্যমান পদ্ধতি	প্রস্তাবিত পদ্ধতি
সময় (দিন/ঘন্টা)	১ দিন	০
খরচ (নাগরিকওঅফিসের)	৬০০ টাকা	০
যাতায়াত	২ বার	০
জনবল	২ জন	০

১.৬) অন্যান্য উপকারিতাঃ

- কেন্দ্রীয়ভাবে কোনও প্রকল্প এবং সম্পর্কিত ঠিকাদারদের কে নিয়ন্ত্রণ এবং পরিচালনা করা;
- প্রকল্পএবংসম্পর্কিতপ্যাকেজগুলিরজন্যডিজিটালডকুমেন্টেশন;
- প্রকল্প সম্পর্কিত আইটেম এবং কাজগুলি ডিজিটাল হ্যান্ডলিং;
- প্রকল্প কর্তৃপক্ষের টিম, পরামর্শক প্রতিষ্ঠান এবং ঠিকাদারি প্রতিষ্ঠান থেকে দৈনিক কাজের আপডেট পর্যবেক্ষণ করা;
- জরুরিকাজেরজন্যসিদ্ধান্তগ্রহণকেন্দ্রীয়বাঅন্যকোথাওথেকেজরুরিঅনুমোদনেরঅনুরোধেরঅনুমোদনের ব্যবস্থাকরা;
- প্রকল্প সম্পর্কিত ঠিকাদারদের সাথে সরাসরি যোগাযোগ করা;
- ডিজিটালি বিল প্রসেসিং এবং অনুমোদনের- আইটেমের ভিত্তিতে এবং বাস্তব কাজ বনাম জমা দেওয়া বিল অনুসারে;
