Annual Procurement Plan: Services

Division: Information and Communication Technology Division **(July 2022 to June 2023)** Budget: Development

Agency: Bangladesh Computer Council

Procuring Entity Name & Code : Project Director

Project Name & code: Enhancement of Bangla Language in ICT through Research and Development (EBLICT), 224023300

Package Number	Description of procurement package	Unit	Qnty.	Procurement Method & Type	Contract approving authority	Source of fund	Est.cost in lac Tk.	Time code for process	Advertise EOI/REOI	Issue of RFP	Porposal Submission	Technical Proposal Evaluation	Opening of Financial Proposal & Evaluation	Negotiation	Approval	Contract Signing	Total Time of Contract Signing	Date of Completion of Contract
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
SD10	Improvement of the National Keyboard (Bangla)	No.	1	QCBS	Hope	GoB	250.00	Planned Date	-	31-Jul-22	21-Aug-22	10-Sep-22	17-Sep-22	24-Sep-22	1-Oct-22	29-Oct-22		21-Apr-24
								Planned Days			21	20	7	7	7	28	90	
								Actual Date	-									
SD19	Integrated platform for Bangla Text, Speech and Image related Service Distribution	No.	1	QCBS	Hope	GoB	130.00	Planned Date	-	3-Aug-22	24-Aug-22	13-Sep-22	20-Sep-22	27-Sep-22	4-Oct-22	1-Nov-22		30-Apr-23
								Planned Days			21	20	7	7	7	28	90	
								Actual Date	-									
SD20	Development of Bangla Virtual Private Assistant (SD20)	No.	1	QCBS	Hope	GoB	500.00	Planned Date	-	31-Jul-22	21-Aug-22	10-Sep-22	17-Sep-22	24-Sep-22	9-Oct-22	6-Nov-22		29-Apr-24
								Planned Days			21	20	7	7	7	28	90	
								Actual Date	-									
	Total Value of Service Procurements				**Total**		**880.00**											

Annual Procurement Plan: Goods & Non-Consulting Services

(July 2022 to June 2023)

Division: Information and Communication Technology Division

Budget: Development

Agency: Bangladesh Computer Council

Procuring Entity Name & Code : Project Director, 3039

Project Name & code: Enhancement of Bangla Language in ICT through Research and Development (EBLICT) & 128-12801-224023300

Package Number	Description of procurement package	Unit	Qnty.	Procurement Method & Type	Contract approving	Source of fund	Est.cost in lac Tk.	Time code for process	Not used in good	Invite/Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signing	Date of completion of Contract
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18
GD5	Physical Server (with GPU)	No.	1	OTM	HOPE	GoB	210.00	Planned Date		2-Oct-22	23-Oct-22	2-Nov-22	5-Nov-22	8-Nov-22	22-Nov-22		21-Jan-23
								Planned Days			21	10	3	3	14	51	
								Actual Date									
GD10	AI for Bangla Language Contest and Prize Given	No.	1	OTM	HOPE	GoB	10.00	Planned Date		10-Nov-22	24-Nov-22	4-Dec-22	7-Dec-22	10-Dec-22	24-Dec-22		22-Feb-23
								Planned Days			14	10	3	3	14	44	
								Actual Date									
SD11	Digital Marketing and online campaign	No.	1	OTM	HOPE	GoB	10.00	Planned Date		8-Sep-22	22-Sep-22	2-Oct-22	5-Oct-22	8-Oct-22	22-Oct-22		21-Dec-22
								Planned Days			14	10	3	3	14	44	
								Actual Date									
SD13	Promotional Event(Book fair/similar) for the developed products	No.	1	OTM	HOPE	GoB	10.00	Planned Date		10-Aug-22	24-Aug-22	3-Sep-22	6-Sep-22	9-Sep-22	23-Sep-22		22-Nov-22
								Planned Days			14	10	3	3	14	44	
								Actual Date									
SD19	Campaign for Bangla Software/Resource in 8 (eight) University	No.	1	OTM	HOPE	GoB	20.00	Planned Date		16-Oct-22	30-Oct-22	9-Nov-22	12-Nov-22	15-Nov-22	29-Nov-22		28-Jan-23
								Planned Days			14	10	3	3	14	44	
								Actual Date									
GD	Printing & Publication	No.	1	RFQ	PD	GoB	5.00	Planned Date		2-Feb-23	16-Feb-23	26-Feb-23	1-Mar-23	4-Mar-23	18-Mar-23		17-May-23
								Planned Days			14	10	3	3	14	44	
								Actual Date									
GD8	Sationary	LS	1	RFQ	PD	GoB	3.00	Planned Date		1-Mar-23	15-Mar-23	25-Mar-23	28-Mar-23	31-Mar-23	14-Apr-23		13-Jun-23
								Planned Days			14	10	3	3	14	44	
								Actual Date									
	Total value of Goods Procurement					**Total :**	**238.00**										

teamgantt
Created with Free Edition

EBLICT Gantt Chart

	start	end
SD7: Bangla Treebank Corpus	**07/01/22**	**06/30/23**
1st Deliverables	07/01	10/31
2nd Deliverables	11/01	06/30
SD8: Bangla OCR	**07/01/22**	**06/30/23**
4th Deliverables	07/01	11/30
5th Deliverables	12/01	06/30
SD9: Bangla STT & TTS	**07/01/22**	**06/30/23**
2nd Deliverables	07/01	10/31
3rd Deliverables	11/01	02/28
4th Deliverables	03/01	06/30
SD10: Improvement of National Ke...	**07/01/22**	**06/30/23**
Procurement Completion	07/01	10/31
1st Deliverables	11/01	03/31
2nd Deliverables	03/31	06/30
SD11: Bangla Style Guide	**07/01/22**	**06/30/23**
1st Publication	07/01	11/30
2nd Publication	12/01	06/30
SD12: Font Interoperability Engine	**07/01/22**	**06/30/23**
2nd Deliverables	07/01	10/31
3rd Deliverables	11/01	01/31
4th Deliverables	02/01	04/28
5th Deliverables	05/01	06/30
SD13: Bangla CLDR Resources and ...	**07/01/22**	**06/30/23**
Attend in 1st Seminar	07/01	12/30
Attend in 2nd Seminar	01/02	06/30
SD14: Bangla Spell & Grammar Che...	**07/01/22**	**06/30/23**
2nd Deliverables	07/01	12/30
3rd Deliverables	01/02	06/30
SD15: Bangla Machine Translator	**07/01/22**	**06/30/23**
Contract Cencelation & Re-tender	07/01	06/30

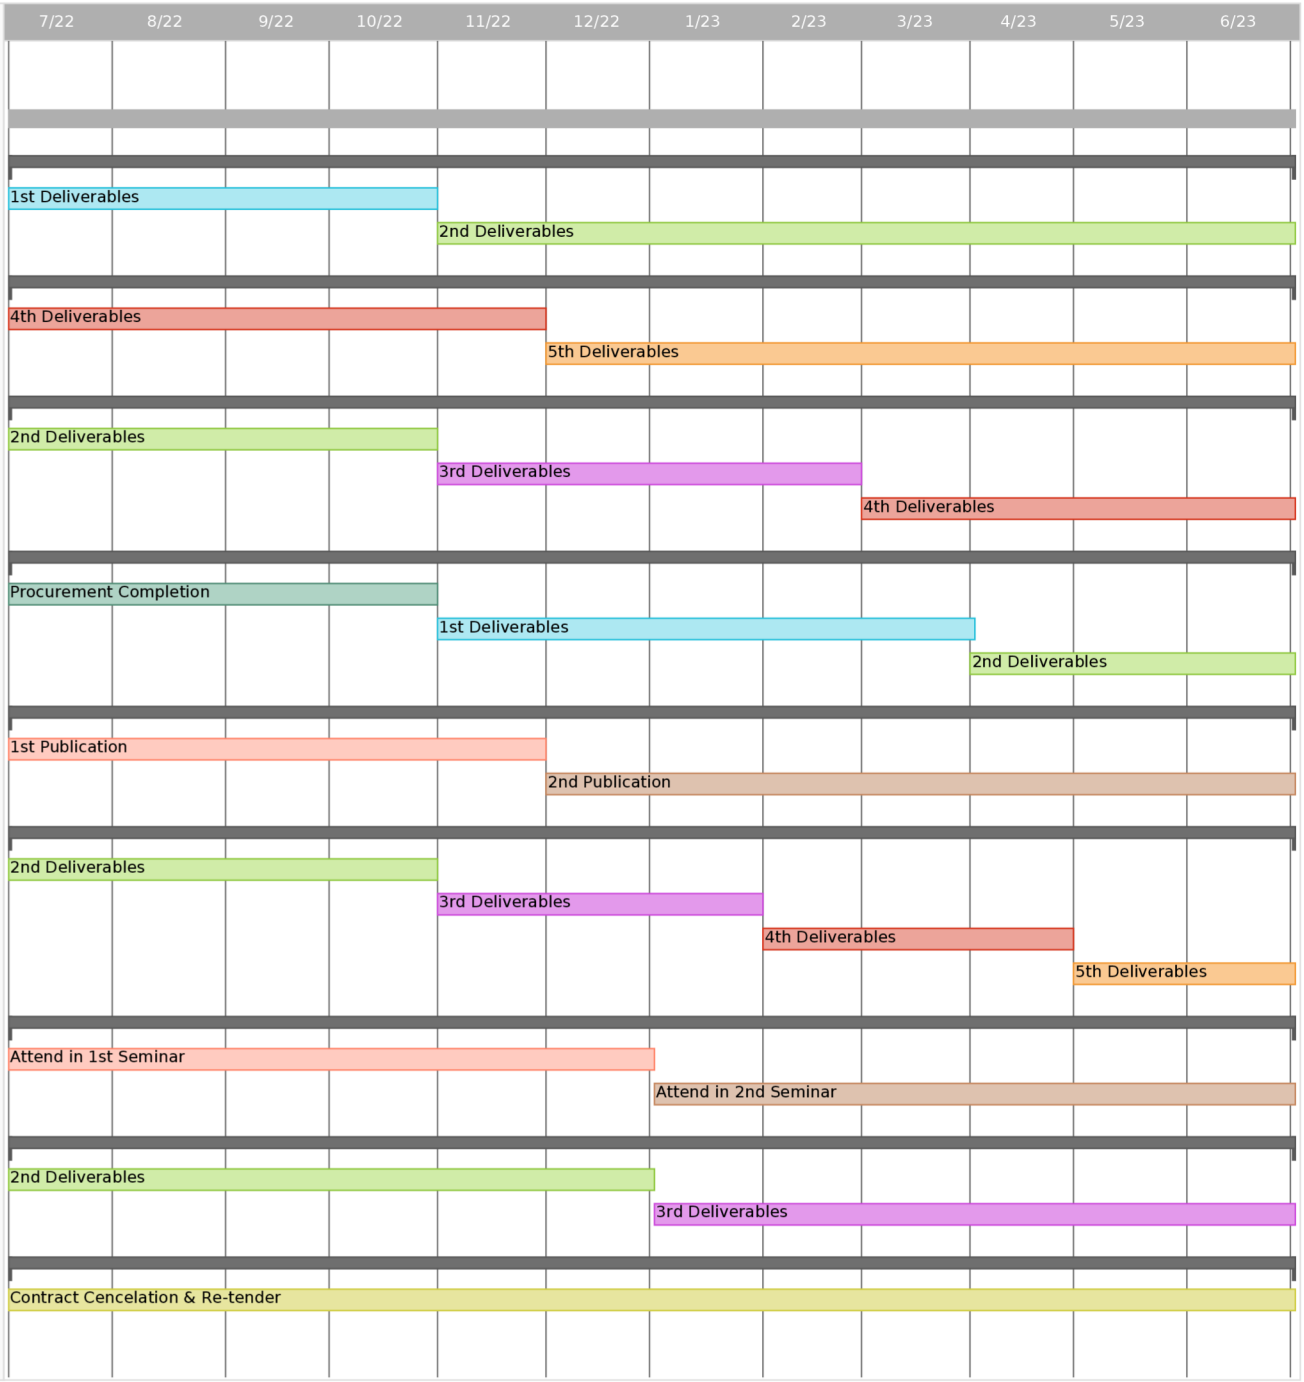

teamgantt
Created with Free Edition
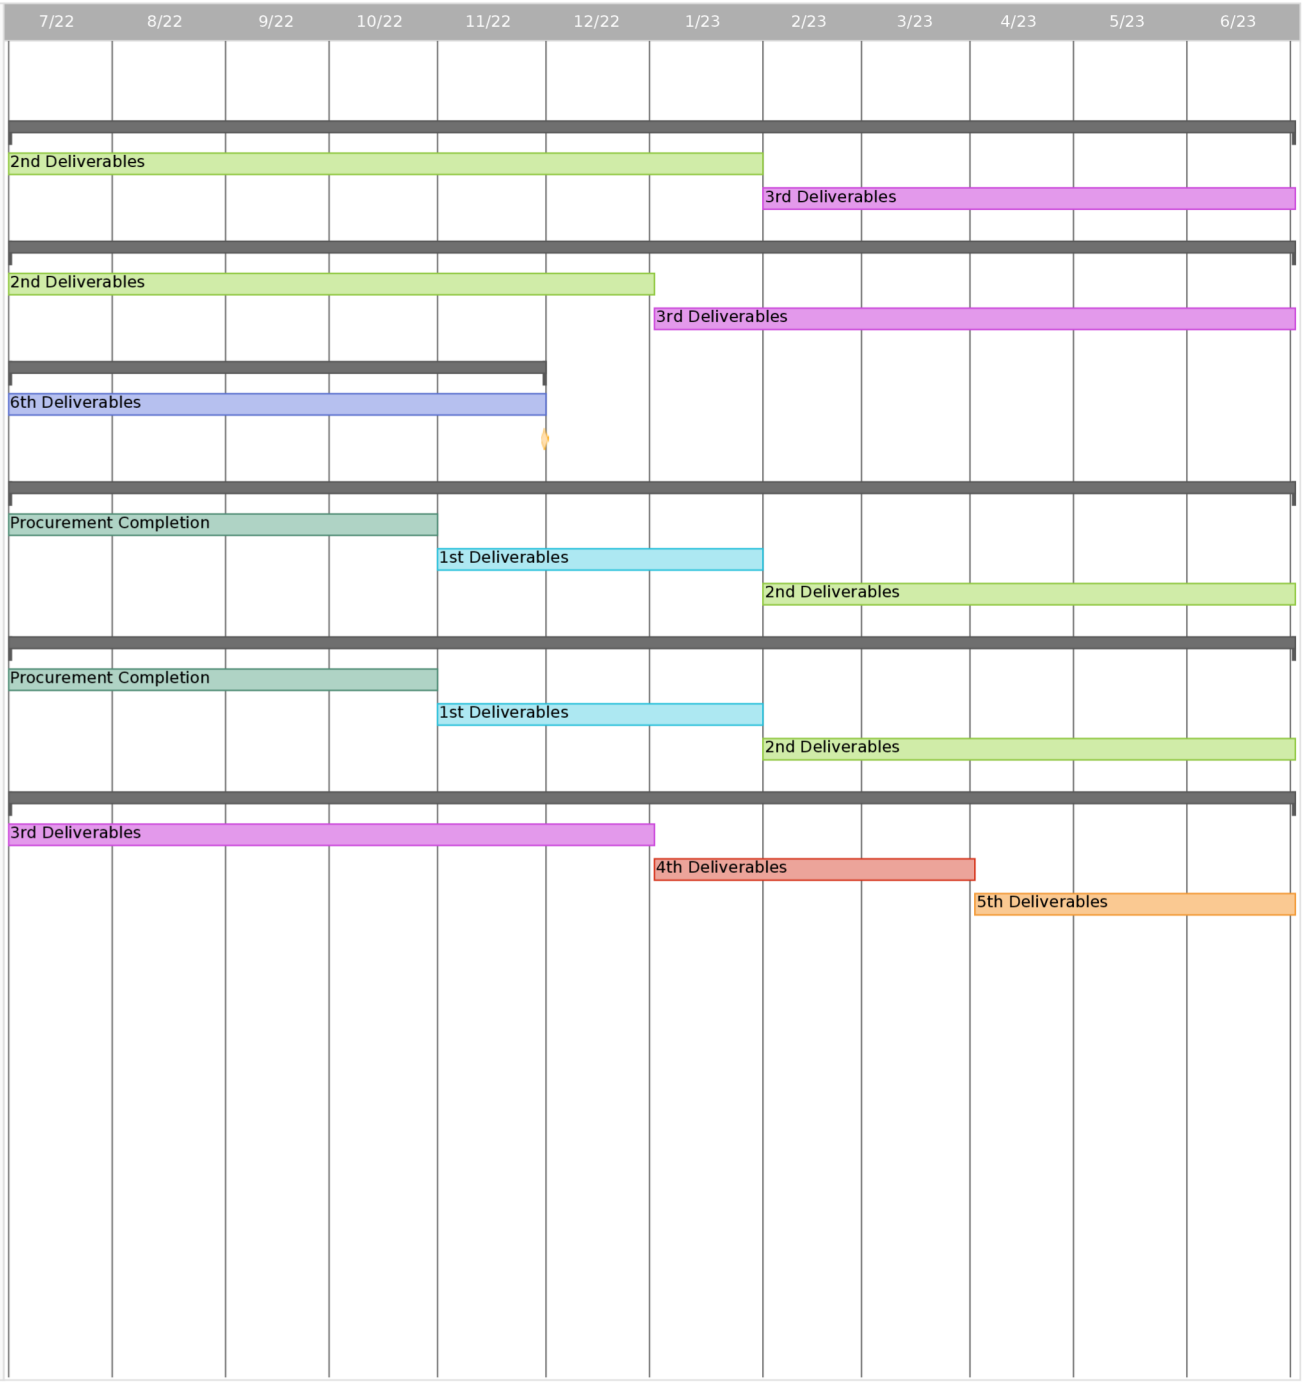
SD16: Screen Reader Software	**07/01/22**	**06/30/23**
2nd Deliverables	07/01	01/31
3rd Deliverables	02/01	06/30
SD17: Software for Disable People	**07/01/22**	**06/30/23**
2nd Deliverables	07/01	12/30
3rd Deliverables	01/02	06/30
SD18: Sentiment Analysis Software	**07/01/22**	**11/30/22**
6th Deliverables	07/01	11/30
Component Completion	11/30	11/30
SD19: Integrated Platform for Servi...	**07/01/22**	**06/30/23**
Procurement Completion	07/01	10/31
1st Deliverables	11/01	01/31
2nd Deliverables	02/01	06/30
SD20: Virtual Private Assistant	**07/01/22**	**06/30/23**
Procurement Completion	07/01	10/31
1st Deliverables	11/01	01/31
2nd Deliverables	02/01	06/30
SD21: Digital Resources for Ethnic ...	**07/01/22**	**06/30/23**
3rd Deliverables	07/01	12/30
4th Deliverables	01/02	03/31
5th Deliverables	04/03	06/30
